

Methodology

Scaffold Module Installation

Multiple Hoist Operation

AS 2550.1-2011 section 6.27.4



NORTH JOHNSON RAIL BRIDGE – SPAN2


GGC Industries



Document Number | **4551 – GGC Methodology – Span 2 – Scaffold Module Installation**

Revision | **01**

Rev	Date	By	Description of Changes
00	19/03/2026	JA	First Issue
01	21/03/2026	CH	Amended lifting points

	Name	Title	Signed	Date
Prepared by	Jerelle Aggabo	Design Engineer		21/03/26
Reviewed by	Harry Butler	Project Manager		21/03/26
Approved by	Clinton Heane	Director		21/03/26


Related Documents

- 4551 – GGC – NJB Bridge - SWMS – REV05
- 4551 – Lift Plan – Span 2 – REV01
- 4551.5_REV01 – North Johnson Lifting Module Design
- 4551.2_REV05 - North Johnson Rail Bridge Span 2 drawings
- GGC-PLN-001 Health & Safety Management Plan
- Relevant client/site emergency procedures

1. Prefabricate Lifting Modules in designated laydon area as per IFC drawings




2. Modules will need to be erected and positioned in correct sequence for correct installation sequence

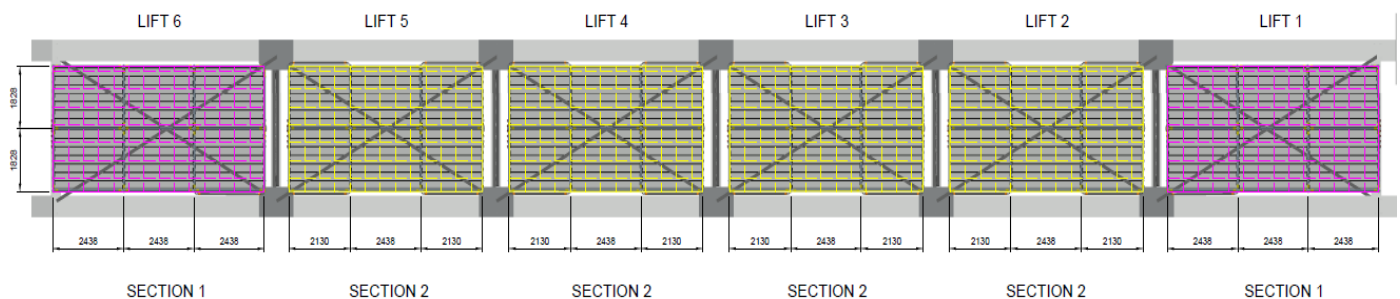

3. Load rail trollies with genset and rigging gear and mobilise into position at the opposite end of span 2. Rail skates will be utilised for this operation
4. Utilising Hi-Rail EWP and rail skates, install static lines on both sides of the train bridge secured to the vertical beams
5. Utilising Hi-Rail EWP, hang 4 x chain block from the bridge beams. The blocks will be hung on 8mm chain snotters in a basket configuration for the bridge.
6. Hang 2 x 10m Inertia reels from bridge beams in between the chain blocks



3.2 TONNES

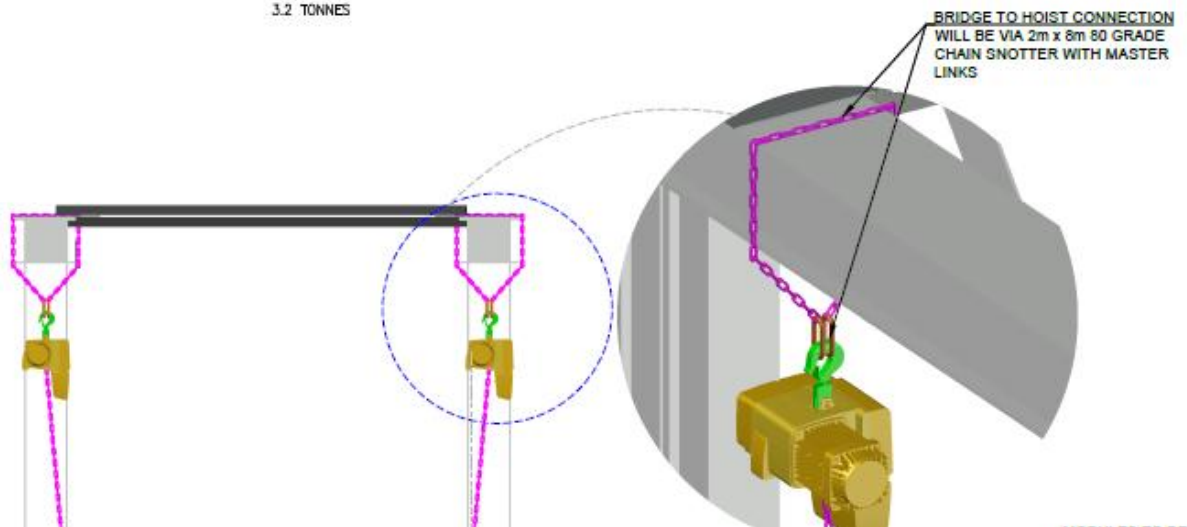

7. Run cabling for chain block to control panel, turn on the genset and run chain blocks confirming correct operations.
8. Inspect all rigging components and attachments and lower chain hooks into position
9. Position 240v, 500kg wick on the train track. This will be dogged down to the bridge structural steel with 2 x 1 tonne lever blocks. Plug into genset, test operation and run out cable



10. Position rail stoppers ready for modules to be lifted onto the tracks



11. Move the franna into position on the drive way to pick up Module 1


12. Rig up module 1 and lift onto track ensuring the scaffold is sitting correctly on its castor wheels



13. Once landed on-track disconnect crane rigging and attach tugger rigging. Take tension, release the rail stoppers and slowly start winching down track and into position for the lift.



14. Once moved into position, attach the chain blocks and take weight on each chain block. Once weight is evenly distributed across the structure, chain blocks to be engaged into “synchronisation mode”

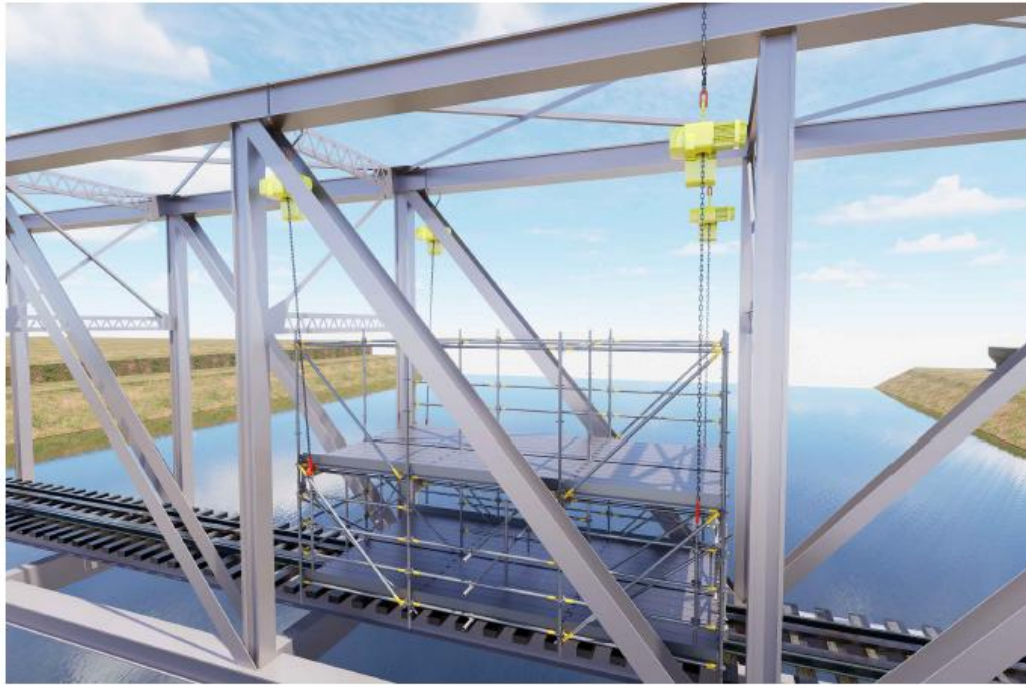

15. Scaffolders to climb onto the module ensuring that this is done internally and connect up to the inertia reels.



16. Once connected, make sure all non-essential personnel are clear of the area.
17. Confirm the lifting team is ready and proceed to lift the moduls into position with the single button control of the 4 x chain blocks.
18. Monitor the chain blocks all the way into position ensuring we have no clash points or contact with structure
19. Once in approximate position, disengage synchro mode and use each chain block on its own to level up the module.



20. Once level, connect the moduels to the bridge beams with beam clamps and tube as per IFC drawings. Any small adjectmenst to level in the cetre bay to be done with a 1 tonne chain block.



21. Once all 8 standards are connected, take weight off the chainblocks and disconnect rigging.
22. Chain blocks can be disconnected from the bridge beams one at a time and moved into the EWP to hang in position ready for the next lift.
23. Temporary bracing, castor wheels and lifting lugs to be removed



24. Lapboards and bracing to be installed and the module is installed and completed.



25. Repeat the process for all six module until all secured in position as per GGC IFC drawings.
26. Install end cantilever bays and connect up to access bays.



27. Inspect scaffold ensuring compliance and 100% fit for purpose and handover to Dynaciv for use



Review and Sign-Off

By signing the below, you acknowledge you have read and understand the rescue emergency response plan and are aware of your obligations should an emergency arise.

Name	Role	Signature	Date
