

Inspection Report

Project	LBST Jetty Pile and Headstock Remediation
Date	10th July 2026
Inspected by	David Edelman
Areas inspected	Pilebent 257 completed, scaffold still in place Pilebent 260 final inspection Pilebent 262 final inspection Pilebent 263 final inspection Pilebent 270 scaffold under construction Pilebent 271 progress inspection Pilebent 273 progress inspection Pilebent 281 progress inspection
Weather conditions	Rain until around 10am then fine. Moderate wind and swell

Purpose of Inspection

- General inspection on pilebents underway and final inspections 260, 262 and 263

Pilebent works

Safety, progress and general observations

- Roadway was very tidy. Less materials/tools stored than at other times. Shipping gallery internals were also neater than previously but can't yet be considered 'neat and tidy'.
- All scaffold decks were encapsulated in accordance with updated SWMS for use of scaffold without kickplates. This has also improved the working environment for welding repairs.
- Lee has been appointed welding supervisor for AAB. A discussion with him noted he is now helping all boilermakers to solve problems and is also overseeing quality etc. This provides further justification for AAB's decision to remove Ingham Agencies. It is evident that Ingham Agencies were providing boilermakers but failed to provide supervision or quality control.
- Benchmark Scaffolding now have a backlog of 4 pilebents to be dismantled. This is likely indicative of the delays caused by poor weather.
- Schedule delays due to weather are likely to be exacerbated by the very large amount of welding on pilebent 271 as well as a delay on Principal direction for pilebent 273.

Pilebent 257 – completed but scaffold still in place

- Scaffold has been available for removal for over a week but has been delayed by poor weather.
- Seashield jacket repair inspected onsite and through dashpivot photos and is satisfactory.
- Clipping of top mesh decks plus bolting and wrapping of ladder feet to be completed following removal of scaffold.

Pilebent 260 – Final inspection

- No defects identified.
- Scaffold may be removed. Bottom deck had already been removed.

Pilebent 262 – Final inspection

- Coating dry film thickness (DFT) measurements

measurement	value	criteria	result
number of spot readings taken	100		
lowest spot measurement	975	≥ 800	PASS
average DFT	1317	≥ 1000	PASS
number of spot measurements below 800	0	0	PASS
number below 1000	1	per % below	
percentage of spot readings below 1000 (allowance is 20%)	1%	$<20\%$	PASS

- Contractor QA process noted some sharp points in the jacket following tightening. Contractor was in process of removing jacket and it was observed, as suspected, that some pieces of gravel from the roadway became included underneath the jacket. This was due to the jacket being prepared with primer on the roadway. The gravel pieces were removed and it was observed that the jacket was not damaged and so was reinstalled.
- Two jacket bolts on the lowest level on Pile 2 were observed to not be fully tightened. Contractor replaced these. Contractor advised to be more careful and slow with use of impact drivers as they cause bolts to gall and seize. Using large ratcheting drive bars is often preferable for the final tightening. It can be a touch slower but overall faster than removing galled bolts.
- Scaffold can now be removed.

Pilebent 263 – Final inspection

- Coating dry film thickness (DFT) measurements

measurement	value	criteria	result
number of spot readings taken	114		
lowest spot measurement	767	≥ 800	FAIL ^
average DFT	1373	≥ 1000	PASS
number of spot measurements below 800	1	0	FAIL ^
number below 1000	5	per % below	
percentage of spot readings below 1000 (allowance is 20%)	4%	$<20\%$	PASS

- ^Area of low thickness was confined to one end of one keeper angle, an area of approximately 10cm x 5cm. Contractor marked the area for touch-up. Note that this is not considered an NCR as the Contractor has agreed to rectify. NCRs will only be raised where the Contractor either can no

longer amend the non-conformance (eg due to scaffold removal) or where the Contractor refuses to do so.

- There was also one other very small area marked up for touch up where jacket installation process had caused minor damage to the coating (not through to steel surface).
- All other tasks completed and inspected with no defects found.
- Following touch-up of low spot and minor damaged area, scaffold may be removed.

Pilebent 270 – Scaffold under construction

- No access

Pilebent 271 – inspection prior to welding repairs

- Pilebent 271 is a headstock only pilebent. It is in very poor condition with very large areas of corrosion as per weld repair sheet supplied 08/07/2026.
- Direction regarding repair patches was to provide full plating on underside. If possible, in 8mm rolled plate in a U-shape.
- The corrosion on the underside was evidently of the deeply pitted variety that cannot be effectively coated without welded repair (see photos)
- The large amount of welded repair on the headstock is likely to cause a schedule delay to the works.
- Gallery feet appear in good condition with likely only jacking and grease injection required.

Pilebent 273 – progress inspection of welding

- Repair plates have been tacked on. Quantity of repairs on this headstock are moderate and will likely be completed in the next week.
- Refer previous inspection report regarding extremely poor condition of gallery feet.
- As welding is close to completion and direction to remediate gallery feet has not yet been provided, there is very likely to be a delay to the works. Remediation works required include cutting off and replacing gallery hooks and feet, and removing and reinstalling brass plates. **Superintendent to provide direction on gallery feet treatment and scheduling of works ASAP**, with options including:
 - a. Contractor to stand-down works on this pilebent following completion of welding works until gallery feet remediation works are approved and effected.
 - b. Contractor to continue with blast and paint works following welding works, without remediating feet. Contractor would then remediate feet following blast and paint, with an additional spot blast and coat to damaged areas.

From a works quality perspective, option b is not recommended. In either option, there will be a delay to the program and additional costs as a result of that delay.

Pilebent 281

- Welding works underway. Works on top and middle deck likely to be completed by Monday.
- Lower deck is not in place to finish welding works as one repair plate requires access to the lower deck.

- Contractor may choose to complete blast and paint on upper deck prior to completing lower deck works.
- Weld quality appears much improved. Weld QA procedure including traceability of welder and inspector will be implemented on this pilebent. This procedure/records have not been observed as yet.
- Welding wire has been changed in accordance with updated weld procedure for AAB. (previous weld procedure was from Ingham agencies). Welding supervisor reports good results achieving 8mm fillet weld in one pass with this wire and new welding equipment.

Action items

Note action items only noted here if they are a direction or require clarification. Items that are simply 'not yet completed' will not be noted.

Item	Who/When
Pilebent 263: Touch up single low area on western end of northern keeper angle to meet specified DFT	AAB prior to removal of scaffold
Pilebent 273: Superintendent to provide direction on gallery feet treatment and scheduling of works	Superintendent/Principal ASAP to minimise delay to works



Photos


1. DFT gauge check

- Accuracy confirmed on 518µm shim on flat steel plate blasted by AAB during the works.
- Rod's DFT gauge and my DFT gauge seem to read differently by around 50 to 100µm with mine reading lower. We need to check them together on a shim or certified thickness standard.
- Both gauges are recently calibrated and are within acceptable error margins. Rod's gauge is 0-5000µm and mine is 0-2000µm range.
- As Contractor is generally easily meeting DFT specification, there is unlikely to be a dispute arising from gauge differences.





2. PB257

- Date painted
- Jacket repair completed

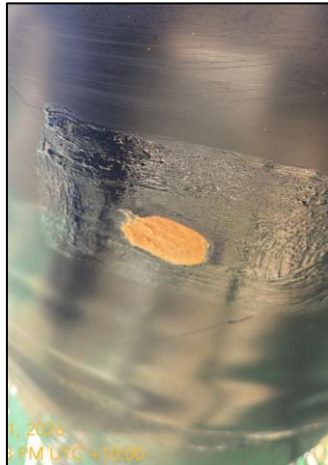


3. PB263 – Final inspection

- Small stones under jacket were removed after being noticed by Contractor QA process
- 2 galled bolts removed and replaced on lower deck

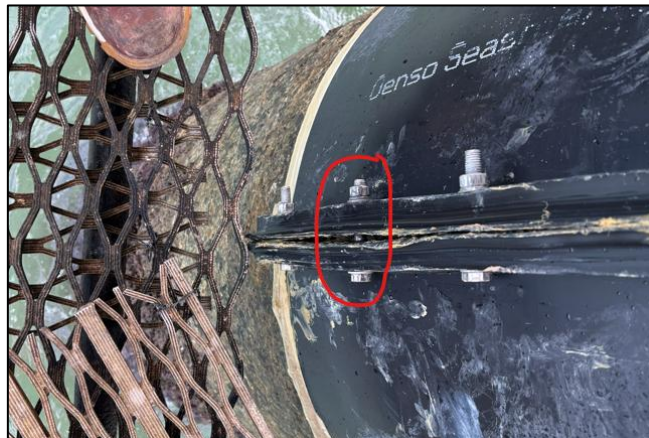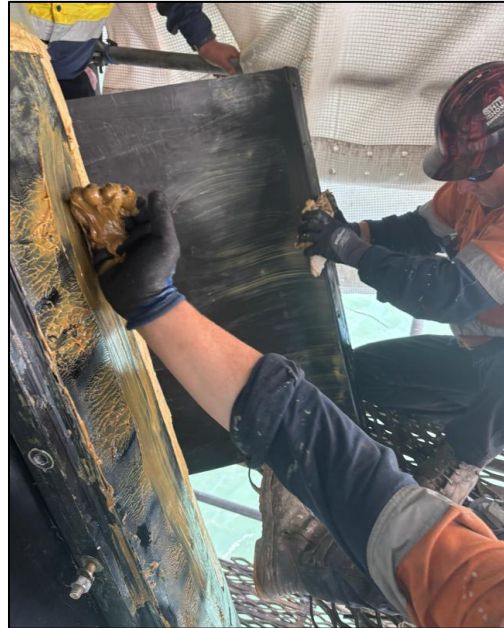



4. PB263 – Final inspection

- One isolated low DFT area marked up for repair

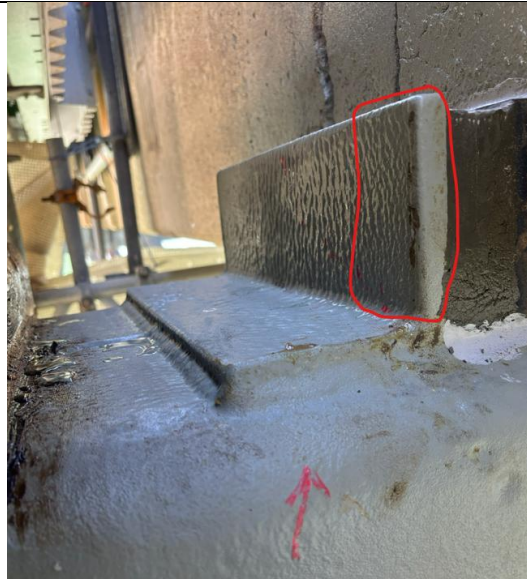

5. PB271 – Awaiting welding

- Large areas of weld repair required
- Deep small pitted/porous areas that can't be painted on underside
- Feet look good (though not fully cleaned)

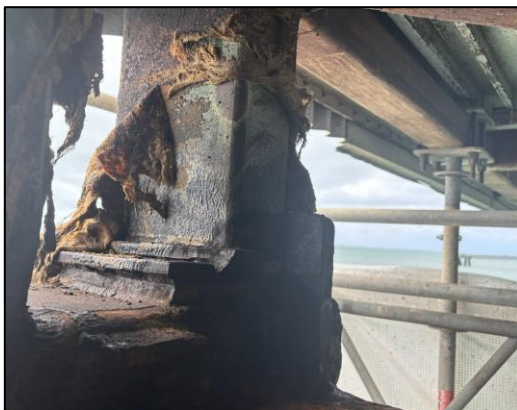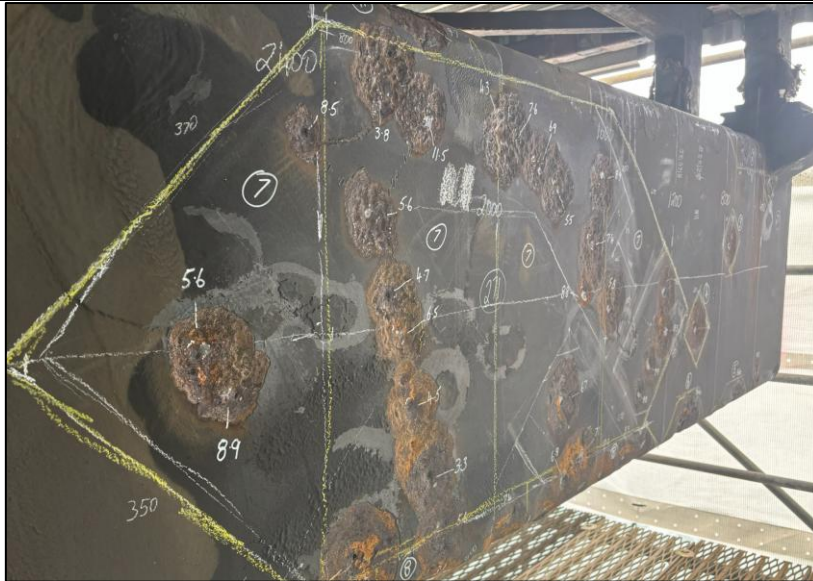

6. PB281 – Welding underway

- Lee supervising and checking quality
- Almost complete on top and middle deck

