

Inspection Report

Project	LBST Jetty Pile and Headstock Remediation
Date	25th July 2026
Inspected by	David Edelman
Areas inspected	Pilebent 270 Welding underway Pilebent 271 abrasive blast and first coat Pilebent 273 progress inspection Pilebent 274 Inspect proposed weld repairs Pilebent 275 progress inspection Pilebent 281 Coating inspection and progress
Weather conditions	Fine and dry. Moderate wind and swell to approx. one metre

Purpose of Inspection

- Blast and paint of pilebent 271
- Final coating inspection on Pilebents 273 and 281
- General inspection on pilebents 270, 274 and 275 underway

Safety, progress and general observations

- All pilebents inspected had encapsulation tied down as required
- Workers on roadway for blast and paint works were observed wearing PFDs
- Benchmark scaffolding were not on site (Saturday)
- Conveyor gallery had been cleared out in preparation for shipping
- Benchmark Scaffolding remain behind on provision of workfronts. While AAB have directed Benchmark to provide additional workfronts in order to accelerate the works, there were only 5 with active workfronts, and these were missing bottom decks. Only two were available for welding works. An additional two pilebents were awaiting removal of scaffold (and PB273 is awaiting direction on gallery leg remediation works).
- Welding progress may be hampered by availability of workfronts over the next week, pending speed of inspection and approval of PB275 headstock repair plates. Contractor has been advised that they may send partial weld mapping through for approval to get repair plate cutting progressing.

Pilebent works

Pilebents 262 and 263

- All works completed but scaffold not yet removed. Not inspected.

Pilebent 270 – Welding in progress

- Welding works are 90% complete
- Abrasive blasting works scheduled Wednesday 29/7

- Water line above works is leaking. Principals to repair or Contractor will redirect leaking water to avoid works.

Pilebent 271 – Abrasive blasting

- Blasting completed around 10:30AM
- A hole along the existing weld was identified at the corner butt weld of the gallery leg shoes following blasting. Some minor weld defects were also found and a small sharp edge. These were found by the Contractor's inspection process. These defects were repaired and the areas reblasted by use of an MBX bristle blaster, with satisfactory cleanliness achieved.
- Weld quality was much improved from previous pilebents with much less porosity and undercutting observed. However, records of weld inspection by the welding supervisor have not been provided as yet. It was indicated that the welding supervisor has carried out checks using a paper-based checklist. A photo of this checklist should be uploaded.

- Climatic conditions prior to paint recorded:

Relative Humidity	50%
Dew Point	11°
Steel surface temperature	22°
Delta	11°
OK to Paint	YES

- Surface preparation tests undertaken:

Sa2.5 blast (visual)	YES – Sa3 achieved
Chloride reading	Less than 1µg/cm ² .
Surface profile average	80µm
OK to Paint	YES

- Mixing of stripe coat mix was observed. 2.5L mix was made. Base was agitated well prior to mixing. The mix was accurately measured in a 5L graduated measuring cup. A flat surface was set up for the purpose. Thinner was added at 4% by measuring 100ml using a small measuring cup.
- Stripe coating was observed and was well performed.
- Mixing of full coat was by full kit mixing.
- Masking of gallery feet was observed. Contractor directed to mask the existing gap between the foot and brass plate and this was completed.
- Commencement of coating was observed.

Pilebent 273 – Awaiting direction on remediation of gallery feet

- Pilebent 273 works are completed excluding wrapping of gallery feet and replacement of top Denso jackets. These works are currently on hold pending direction on remediation of gallery feet.
- Coating dry film thickness (DFT) measurements

measurement	value	criteria	result
number of spot readings taken	100		
lowest spot measurement	932	>= 800	PASS
average DFT	1351	>= 1000	PASS
number of spot measurements below 800	0	0	PASS
number below 1000	6	per % below	
percentage of spot readings below 1000 (allowance is 20%)	6%	<20%	PASS

- No defects observed.

Pilebent 274 – Inspection of proposed repair plates

- Proposed repair plates are appropriate. One small extra plate will be requested at the edge of repair plate 15.
- Verbal direction was provided to progress with cutting of repair plates as drawn and additional plate can be a small addition.
- PB274 is an anchor bent and does not have sliding gallery feet
- There is a section on the underside of the lower headstock that has not yet been inspected as the scaffold mid-level is not constructed. AAB to send through inspection report for underside once scaffold is built.

Pilebent 275 – Prior waterblast

- Had not yet been waterblasted
- Filter mesh on floor was in the process of being set up. Waterblasting commenced later that day but was not completed on time for reinspection.
- Pilebent 275 does not have sliding feet.
- The Denso tape encapsulation of the gallery feet is very dry externally. Suggest that when the tape is partially removed under the contract (~300mm from headstock top face), full removal is carried out if the tape is observed to be dry. The age of this tape may be 30 years+ and exposed to sunlight, so it likely needs replacement up to gallery level. This tape can be reached as part of JMV-based maintenance activities, so tape can be left as-is if still providing protection.
- Contractor to report on condition of tape during removal.

Pilebent 281 – progress inspection

- Blasting and painting main works have been completed.
- Works underway include completion of one repair plate low down on one pile. Waves were restricting access to the lowest deck to complete these works. Pile jackets for all 6 piles will be applied following completion of scaffold bottom deck.
- There will be extensive coating touch up works at scaffold support areas. These areas will be completed as scaffold lower decks are removed and as scaffold is progressively dismantled.

Contractor to carry out robust QA on these areas. Scaffold support points have been areas of coating breakdown on previous projects.

- Coating dry film thickness (DFT) measurements

measurement	value	criteria	result
number of spot readings taken	132		
lowest spot measurement	917	>= 800	PASS
average DFT	1250	>= 1000	PASS
number of spot measurements below 800	0	0	PASS
number below 1000	6	per % below	
percentage of spot readings below 1000 (allowance is 20%)	5%	<20%	PASS

Action items

Note action items only noted here if they are a direction or require clarification. Items that are simply 'not yet completed' will not be noted.

Item	Who/When
Principal to tighten leaking water line above PB270	Principal, ideally prior to abrasive blasting works on Wednesday 29/7
Contractor to attach weld inspection records to Dashpivot QA system, showing inspection of each welded plate and pad weld and who the inspector was.	AAB
Superintendent to provide direction re PB273 gallery sliding feet	Superintendent, ASAP to minimise delay costs
Contractor requested to take photos and provide report on condition of Denso tape on pile bent 275 gallery legs during removal.	AAB

Photos

1. PB270 – abrasive blasting and painting


- Very clean blast
- Hole along weld not visible until blasting was completed. Was repaired and reblasted prior to coating
- Stripe coating carried out
- Masking of gap between sliding foot and brass plate






2. PB273


- Coating completed but awaiting direction on severely damaged gallery leg

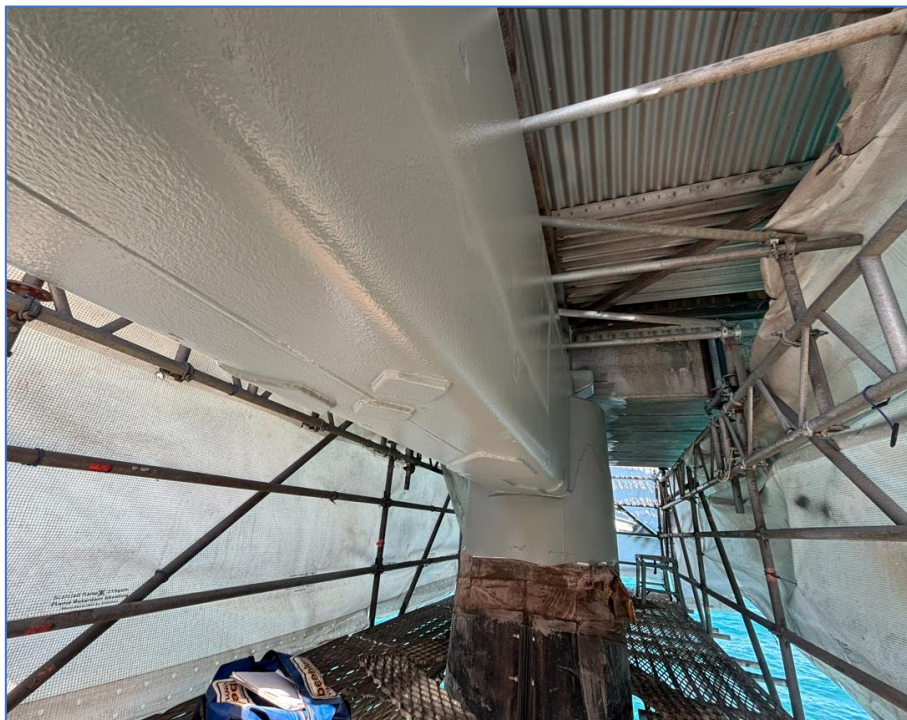

3. PB274 – Weld patches proposed

- Patches approved
- Additional patch adjacent to patch 15
- PB274 is a good example of where an allowance of 8mm vertical edge plates (rather than 45 degree angle) on northern end of headstock may allow reduced repair plate qty. It has extensive low areas in a vertical line. These are better treated as one large plate with the 45 degree requirement but may be smaller plates if vertical edges were accepted.

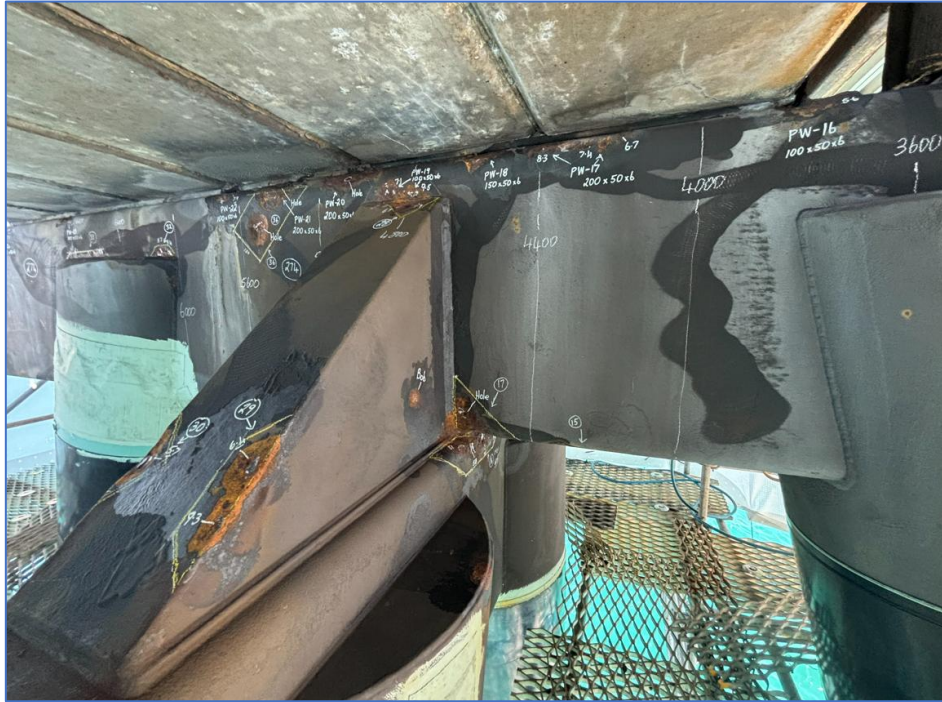

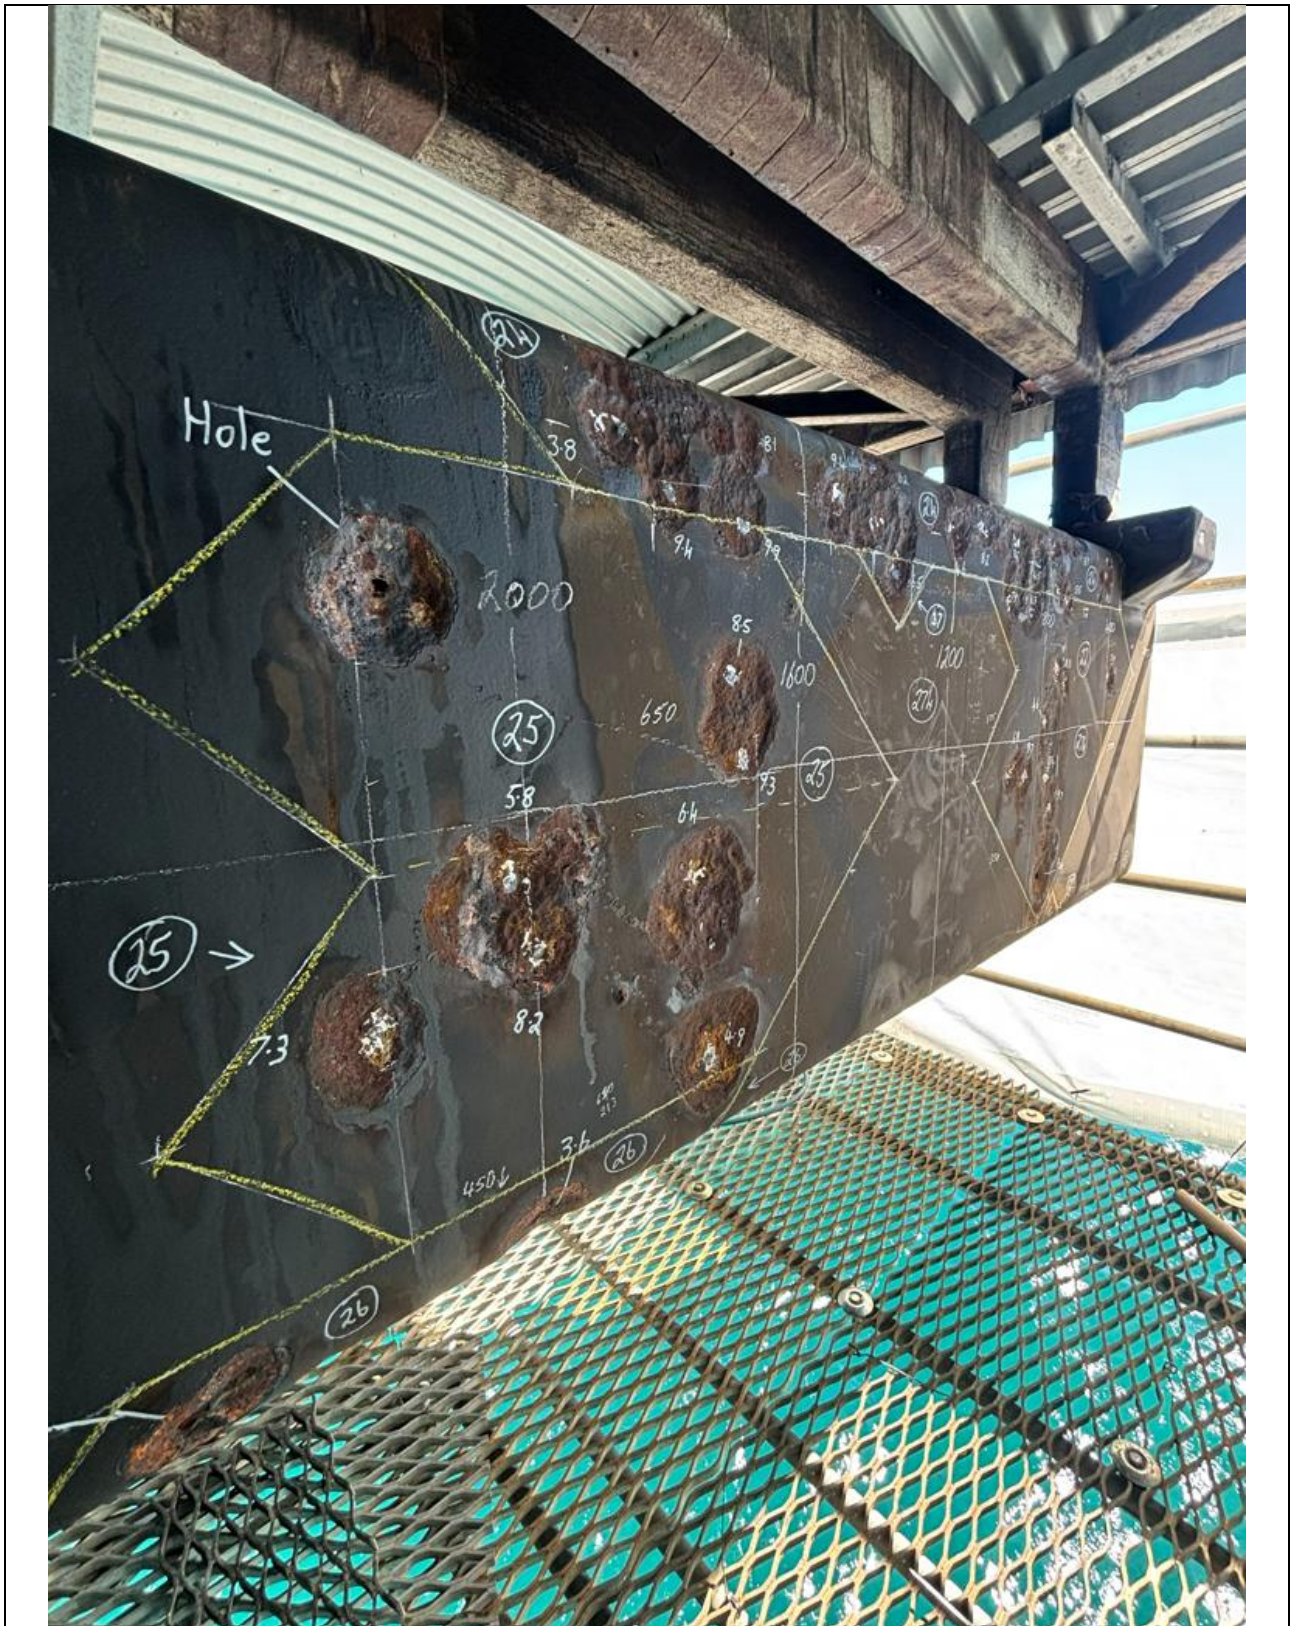

4. PB275 – prior waterblasting

- Extensive corrosion
- Denso tape on gallery legs is dry but feels like it might still be OK underneath



5. PB281 – main coating completed, piles underway

- Will be lots of coating touch up points where scaffold prevented coating. This problem is unique to this pilebent and therefore was accepted at time of tender. Generally scaffold design was developed to avoid touching headstocks.
- Piles underway – require last bit of welding from bottom deck and completion of bottom deck scaffold build before jackets can be completed.

